

RPA Hospital Redevelopment

Construction update 31 March 2025

Work is progressing on the east campus to ready the site for the future 15-storey hospital building located on Lambie Dew Drive.

Johns Hopkins Drive

- Reopened on Friday 21 March 2025.
- Vehicle access to Centenary Institute, Kerry Packer Education Centre and Molecular Imaging is now via Johns Hopkins Drive only.

RPA Hospital loading dock

- Access will remain via Gloucester House Drive and there will be no through road to Johns Hopkins Drive via Lambie Dew Drive.

Missenden Road

- Work on Missenden Road footpath commenced on Wednesday 26 March 2025, the works were paused on Thursday to ensure pedestrians are appropriately managed around the diversion. It is expected that these works will recommence from early April. The works involve a section of the Missenden Road footpath outside the Emergency Department drop-off area being closed for approximately six weeks to enable the installation of in-ground infrastructure for the new hospital.
- There will be detours in place to help pedestrians safely navigate around the works.
- The works zone will be demobilised daily, enabling pedestrians to utilise the Missenden Rd footpath out of Construction hours


Internal refurbishment Works

- Demolition and refurbishment work continues as we reconfigure spaces for the future East expansion.
- There will be upcoming works in the corridor and atrium space on Level 4 and we will provide relevant plans once the works have been confirmed.

We thank you for your continued support of the RPA Hospital Redevelopment.



Date	Works	Location	Impacts
Overview of current and upcoming activities			
Expected to commence 5 April 2025	East Gas Compound Crane Lift	East campus	<ul style="list-style-type: none"> East gas compound crane lift Pedestrian impacts Centenary Institute access impacts Exclusion zone in place for duration of works
Expected to commence in early April 2025	Pedestrian and vehicle changes Works notice	East campus	<ul style="list-style-type: none"> Missenden Road footpath closure and detour for approximately six weeks No through road between Lambie Dew Drive and Johns Hopkins Drive
From 7 January 2025	Loading dock access Works notice	Johns Hopkins Drive	<ul style="list-style-type: none"> Loading dock access via Gloucester House Drive only No through road between Johns Hopkins Drive and Lambie Dew Drive Loading dock bays 3 and 4 closed
Ongoing	Piling works Works notice	Lambie Dew Drive and Johns Hopkins Drive	<ul style="list-style-type: none"> Piling works commenced for eastern extension located west of the Susan Wakil Building Intermittent noise and vibration from piling work
Ongoing	Asbestos removal Fact sheet	Lambie Dew Drive	<ul style="list-style-type: none"> Asbestos removal inside established construction site Qualified asbestos removal workers in Personal Protective Equipment (PPE) will complete the works Air monitoring and reporting in place

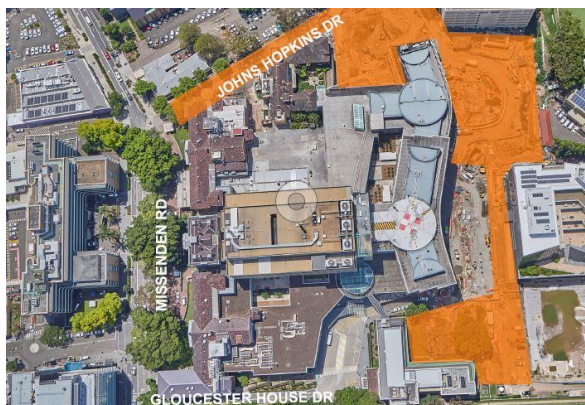

Scan here

To go to our interactive map and see where construction works are occurring on site.

Minimising construction impacts

The health and safety of staff and the local community are our main priorities. Please note the timing of works is subject to change and we will continue to keep you informed as works progress.

Stay up to date on the redevelopment by [subscribing](#) to our project updates and visit our project website rparedevelopment.health.nsw.gov.au for more information.

Email RPAREdevelopment@health.nsw.gov.au or phone (02) 9978 5901 with any questions.

The RPA Redevelopment Team
