

RPA Hospital Redevelopment

Construction update 13 February 2025


Works are progressing on the east campus in preparation for the construction of the 15-storey hospital building. The first tower crane is now in place on Lambie Dew Drive and a second tower crane is expected to be installed near Johns Hopkins Drive in mid-2025. Both cranes will remain operational for approximately two years, facilitating the major construction work ahead.

Access to the RPA Hospital loading dock remains via Gloucester House Drive, as Johns Hopkins Drive is temporarily closed for the installation of new in-ground electrical infrastructure.

Inside the existing hospital, demolition and refurbishment works are underway to reconfigure spaces in preparation for the new facility. Meanwhile, piling works continue near Lambie Dew Drive to support the future hospital expansion.

Please note, a planned power outage will affect the RPA Hospital Staff and Visitor Car Park on Tuesday, 18 February, and Saturday, 22 February 2025. These outages will coincide with scheduled Ausgrid works in the Queen Mary car park.

Date	Works	Location	Impacts
Current and upcoming activities overview			
On 18 February and 22 February 2025	RPA Hospital Staff and Visitor Car Park power outage Works notice	RPA Hospital Staff and Visitor Car Park	<ul style="list-style-type: none"> Planned power outage between 6am to 7am on Tuesday 18 February and between 5am to 4pm Saturday 22 February 2025 Ausgrid maintenance works in the Queen Mary car park on Tuesday 18 February
From 18 January 2025 ongoing	Tower crane installation Works notice	Lambie Dew Drive	<ul style="list-style-type: none"> Tower crane installed on Lambie Dew Drive In use for approximately two years to help construct the future 15-storey building at RPA Hospital Increase of construction traffic and deliveries
From 7 January 2025	Loading dock access Works notice	Johns Hopkins Drive	<ul style="list-style-type: none"> Loading dock access via Gloucester House Drive only No through road between Johns Hopkins Drive and Lambie Dew Drive Loading dock bay 3 and 4 closed
From 7 January 2025	Johns Hopkins Drive road closure Fact sheet	Johns Hopkins Drive	<ul style="list-style-type: none"> Johns Hopkins Drive full road closure RPA Hospital loading dock access and Centenary Institute vehicle access via Gloucester House Drive only No through road between Lambie Dew Drive and Johns Hopkins Drive
Ongoing	Piling works Works notice	Lambie Dew Drive and Johns Hopkins Drive	<ul style="list-style-type: none"> Piling works commenced for eastern extension located west of the Susan Wakil Building Intermittent noise and vibration from piling work
Ongoing	Asbestos removal Fact sheet	Lambie Dew Drive	<ul style="list-style-type: none"> Asbestos removal inside established construction site Qualified asbestos removal workers in Personal Protective Equipment (PPE) will complete the works Air monitoring and reporting in place

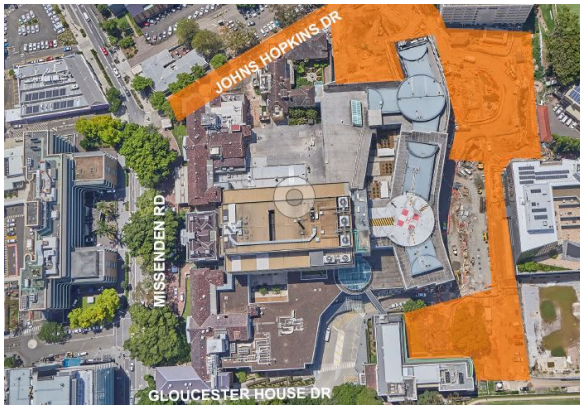

Scan here

To go to our interactive map and see where construction works are occurring on site.

Minimising construction impacts

The health and safety of staff and the local community are our main priorities. Please note the timing of works is subject to change and we will continue to keep you informed as works progress.

Stay up to date on the redevelopment by [subscribing](#) to our project updates and visit the project website rparedevelopment.health.nsw.gov.au for more information.

Email RPAREdevelopment@health.nsw.gov.au or phone (02) 9978 5901 with any questions.

The RPA Redevelopment Team
